


Activity ID	Activity Name	Start	Finish	2009					2010				2011				
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
LC06c Tributary Barrier Removal		05-14-07 A	09-28-07														
Conceptual - Resource Plan		05-14-07 A	09-05-07 A	- Resource Plan													
LF9910	Prepare for 2nd LCFF meeting for tributary barriers	05-14-07 A	05-25-07 A														
LF9920	2nd LCFF meeting, determine next component for tri...	06-08-07 A	06-08-07 A														
LF9930	Prepare for 3rd LCFF meeting for tributary barriers	06-08-07 A	07-06-07 A														
LF9940	3rd LCFF meeting, determine next component for trib...	09-05-07 A	09-05-07 A														
Planning		04-23-08	01-30-09	01-30-09, Planning													
LF9960	Field tour to inspect tribs	04-23-08*	04-23-08														
LF9970	Determine first two tribs for treatment	04-24-08	05-03-08														
LF9950	Obtain Contract for Design of tributary barrier removals	05-05-08	01-30-09														
Execution		02-04-09	12-10-14														
Tribs 1 & 2		02-04-09	12-17-10	12-17-10, Tribs 1 & 2													
LF1390	Consultant Designs tributary barrier removals 1&2	02-04-09	06-09-09														
LF1450	Obtain Permit for Tributary Barriers 1&2	05-08-09	05-07-10														
LF1460	Go out for bid on Trib Barriers ALL	05-07-10	09-24-10														
LF1400	Two site construction 1&2	09-24-10	12-17-10														
Tribs 3 & 4		11-08-10	12-12-11														
LF1420	Designs tributary barrier removals 3&4	11-08-10	06-06-11														
LF1470	Obtain Permit for Tributary Barriers 3&4	11-08-10	06-06-11														
LF1430	Two site construction 3&4	09-19-11	12-12-11														
Tribs 5 & 6		11-01-11	12-10-12														
LF1490	Designs tributary barrier removals 5&6	11-01-11	05-28-12														
LF1500	Obtain Permit for Tributary Barriers 5&6	11-01-11	05-29-12														
LF1510	Two site construction 5&6	09-18-12	12-10-12														
Tribs 7 & 8		10-31-12	12-10-13														
LF1520	Designs tributary barrier removals 7&8	10-31-12	05-28-13														
LF1530	Obtain Permit for Tributary Barriers 7&8	10-31-12	05-28-13														
LF1540	Two site construction 7&8	09-18-13	12-10-13														
Tribs 9 & 10		10-31-13	12-10-14														
LF1550	Designs tributary barrier removals 9&10	10-31-13	05-28-14														
LF1560	Obtain Permit for Tributary Barriers 9&10	10-31-13	05-28-14														
LF1570	Two site construction 9&10	09-18-14	12-10-14														

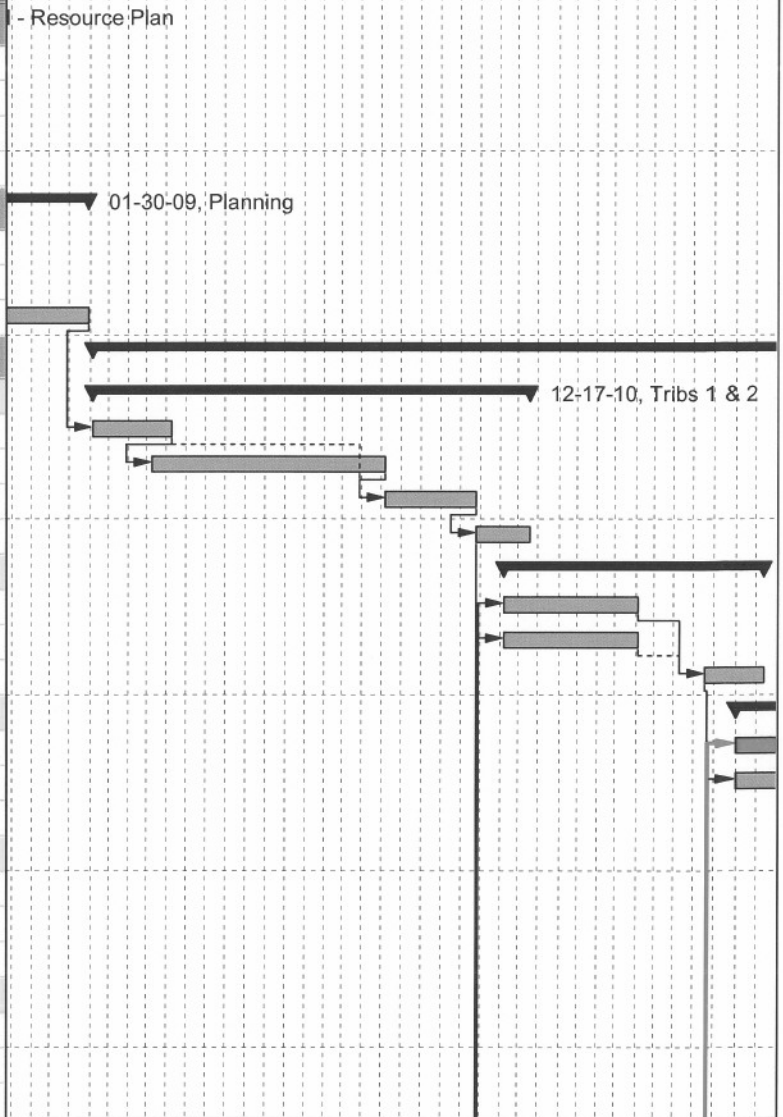

Actual Work
 Remaining Work
 Critical Remaining Work
 Summary
 ◆ Milestone

Activity ID	Activity Name	Start	Finish	2009				2010				2011								
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
Monitoring & Evaluation		11-05-10	09-28-57																	
LF1410	Evaluation Trib Barriers 3 & 4	11-05-10	11-08-10																	
LF1480	Evaluation Trib Barriers 5 & 6	10-31-11	11-01-11																	
LF1440	Monitor Trib 1&2	11-01-11	11-01-11																	
LF1580	Monitor Trib 1-4	10-30-12	10-30-12																	
LF1590	Evaluation Trib Barriers 7 & 8	10-30-12	10-30-12																	
LF1600	Monitor Trib 1-6	10-30-13	10-30-13																	
LF1610	Evaluation Trib Barriers 9&10	10-30-13	10-30-13																	
LF1620	Monitor Trib 1-8	10-30-14	10-30-14																	
LF1630	2014 Monitor all Tribs assume every 3rd year	10-30-15	11-02-15																	
LF1780	2017 Monitor all Tribs assume every 3rd year	10-29-18	10-30-18																	
LF1650	2020 Monitor all Tribs assume every 3rd year	10-26-21	10-27-21																	
LF1750	2023 Monitor all Tribs assume every 3rd year	10-23-24	10-24-24																	
LF1730	2026 Monitor all Tribs assume every 3rd year	10-21-27	10-22-27																	
LF1720	2029 Monitor all Tribs assume every 3rd year	10-18-30	10-21-30																	
LF1710	2032 Monitor all Tribs assume every 3rd year	10-17-33	10-18-33																	
LF1700	2035 Monitor all Tribs assume every 3rd year	10-14-36	10-15-36																	
LF1690	2038 Monitor all Tribs assume every 3rd year	10-12-39	10-13-39																	
LF1640	2041 Monitor all Tribs assume every 3rd year	10-09-42	10-10-42																	
LF1680	2044 Monitor all Tribs assume every 3rd year	10-06-45	10-09-45																	
LF1670	2047 Monitor all Tribs assume every 3rd year	10-05-48	10-06-48																	
LF1660	2050 Monitor all Tribs assume every 3rd year	10-03-51	10-04-51																	
LF1760	2053 Monitor all Tribs assume every 3rd year	09-30-54	10-01-54																	
LF1770	2056 Monitor all Tribs assume every 3rd year	09-27-57	09-28-57																	

Actual Work
 Critical Remaining Work
 Summary
 Remaining Work
 Milestone
