




Chelan – Manson 115 kV Transmission Line

Proposed Fire Hardening
Project Update

December 16, 2019

Most Recent Outreach

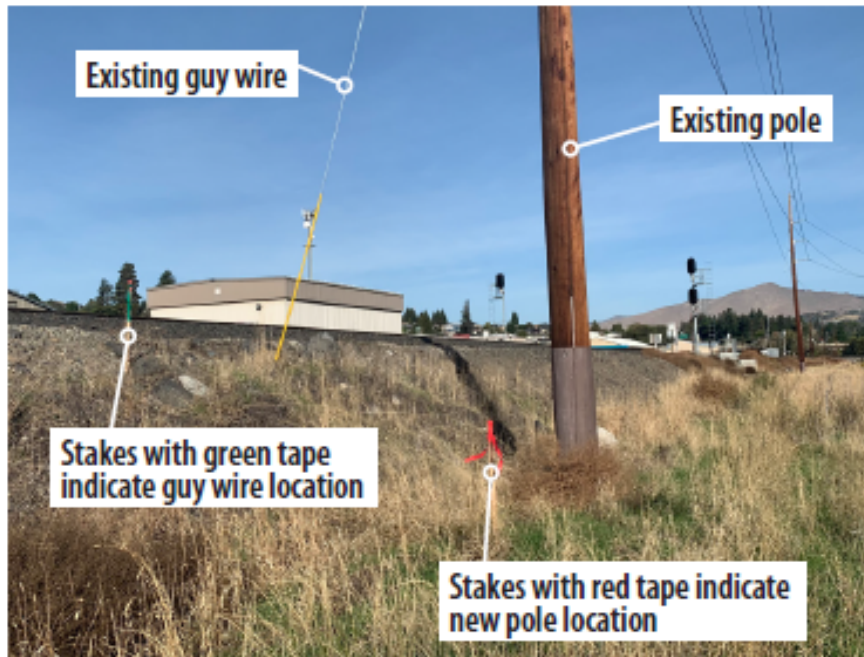

PREGUNTAS? Si tiene preguntas en español por favor llame al (509) 661-4081 o mande sus preguntas a contactus@chelanpud.org

Questions?

If you have questions or comments about the project, or would like a map of the poles included in this project that are on or near your property, please reach out to Jenna Rahm at jenna.rahm@chelanpud.org or call (509) 661-4630.



- **Mid-October:** Pole staking postcards sent to property owners to inform them of staking
- **Mid-October:** Letter sent to a larger group of stakeholders with 30% Design details
- **Late October:** Pole staking performed on landowner property
- **Nov 20:** Drop-in session at Chamber of Commerce – no feedback received
- **Nov 26:** City Council Update – no feedback received
- **To-date:** No feedback received from postcard mailers



Next Steps


- **Based** on feedback received (or lack thereof), will proceed with option to rebuild from Chelan Falls Switchyard to Union Valley Substation.
- **\$5M** budget has been approved
- **Mid-December:** Send letter informing residents of plan to move forward with the larger project

Anticipated Timeline

- December 2019: Complete outreach with letter to residents informing of plan to move forward with complete rebuild
- 2020: Design and procure
- 2021: Construction

Current planning condition:

We are here now

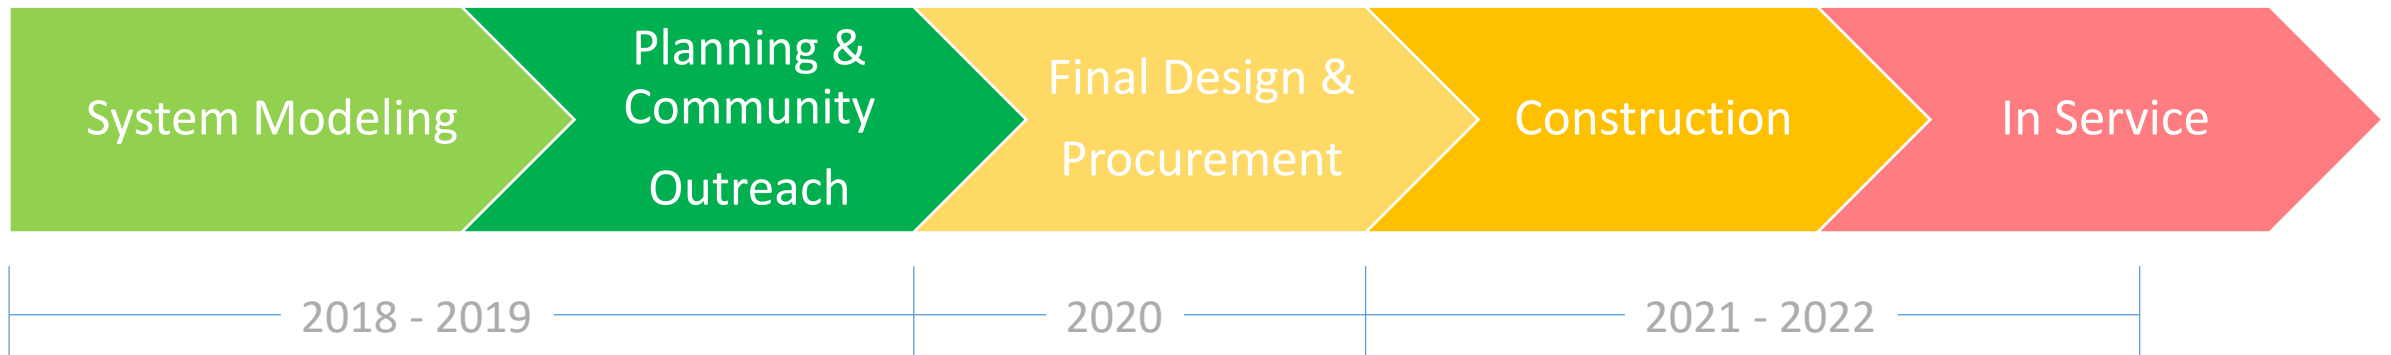

Questions?

